



Project
Leaders



Grey County LTC Redevelopment Projects

Long-Term Care Redevelopment Task Force Update
October 12, 2021


Grey County – LTC Redevelopment Projects

Summary of Key Decisions

- Approval to Proceed with the RFP for a Prime Consultant;
- Prime Consultant's scope revised to the Rockwood Terrace LTC Redevelopment Project only;
- Prime Consultant's scope revised to include the preparation of an alternative conceptual Master Plan for the Campus of Care.

Grey County – LTC Redevelopment Projects

Overall Schedule – Rockwood Terrace

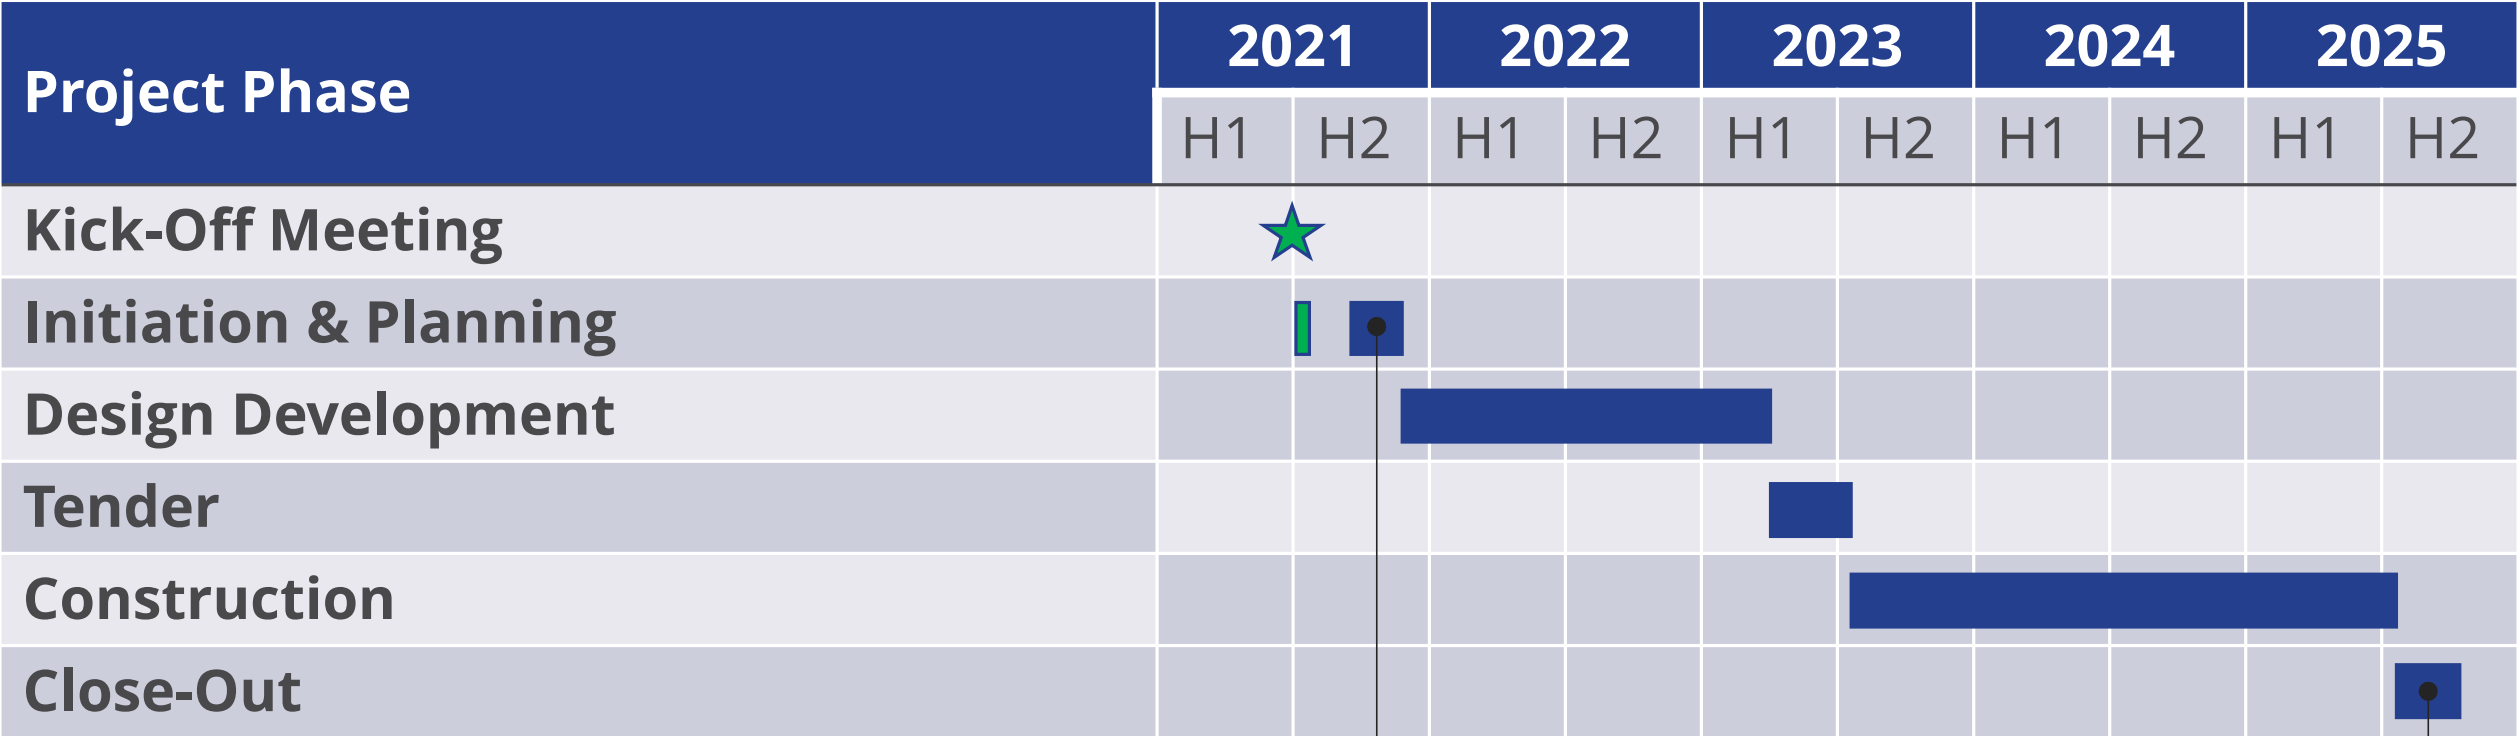

█ Actual
█ Ongoing / Forecast

Prime Consultant RFP Issued on September 7th, 2021

First Resident Date Milestone: July 2025

Grey County – LTC Redevelopment Projects

Prime Consultant Procurement - Timeline

Activity	Date / Duration
Draft RFP Documents issued to Grey for Review	June 30 th , 2021
Review Comments with Grey	July 21 st , 2021
Issue RFP, Manage Q&A and Issue Addenda	Sep 7 th - Oct 7 th , 2021
Receive and Review Submissions	Oct 7 th – Nov 4 th , 2021
Interviews	October 25 th , 2021
LTC Redevelopment Task Force Approval of Prime Consultant Selection	November 4 th , 2021
Council Approval of Prime Consultant Selection	November 12 th , 2021
Kick-off Meeting with Prime Consultant	November 15 th , 2021
